




1-5 HOMESTEAD DRIVE, STAPYLTON
CONTRACT PROGRAMME

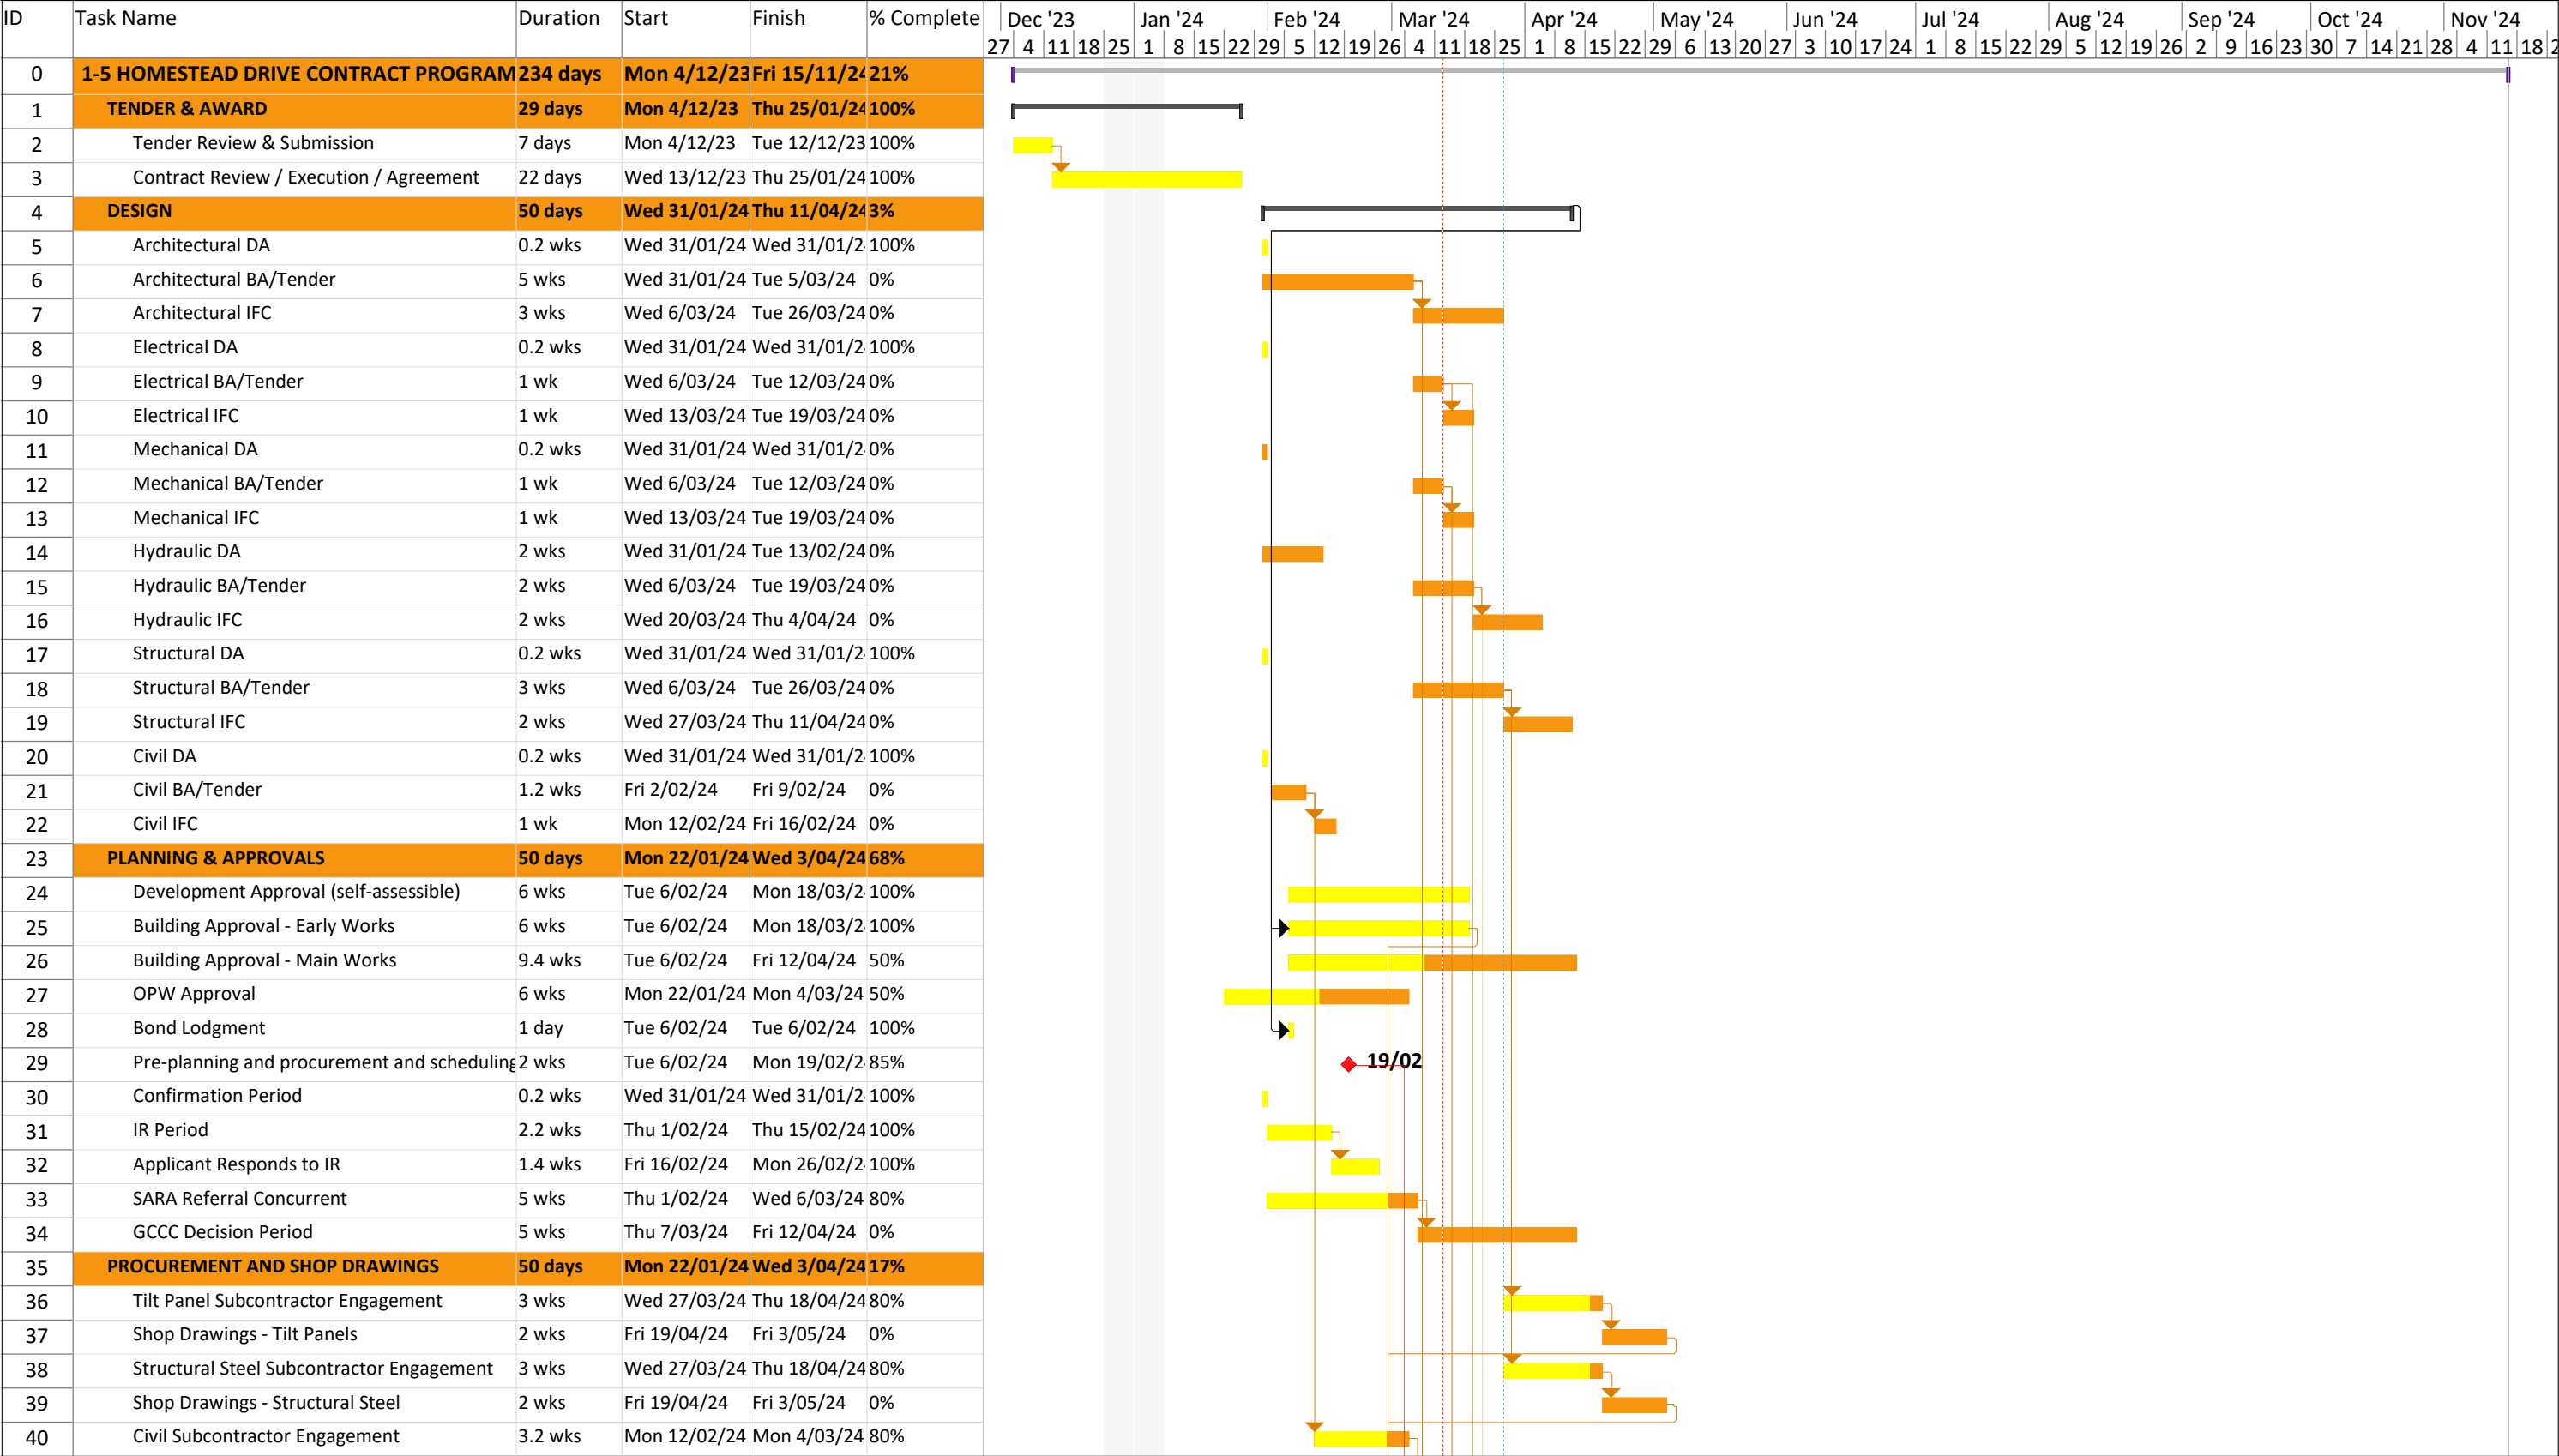

1-5 HOMESTEAD DRIVE, STAPYLTON
CONTRACT PROGRAMME

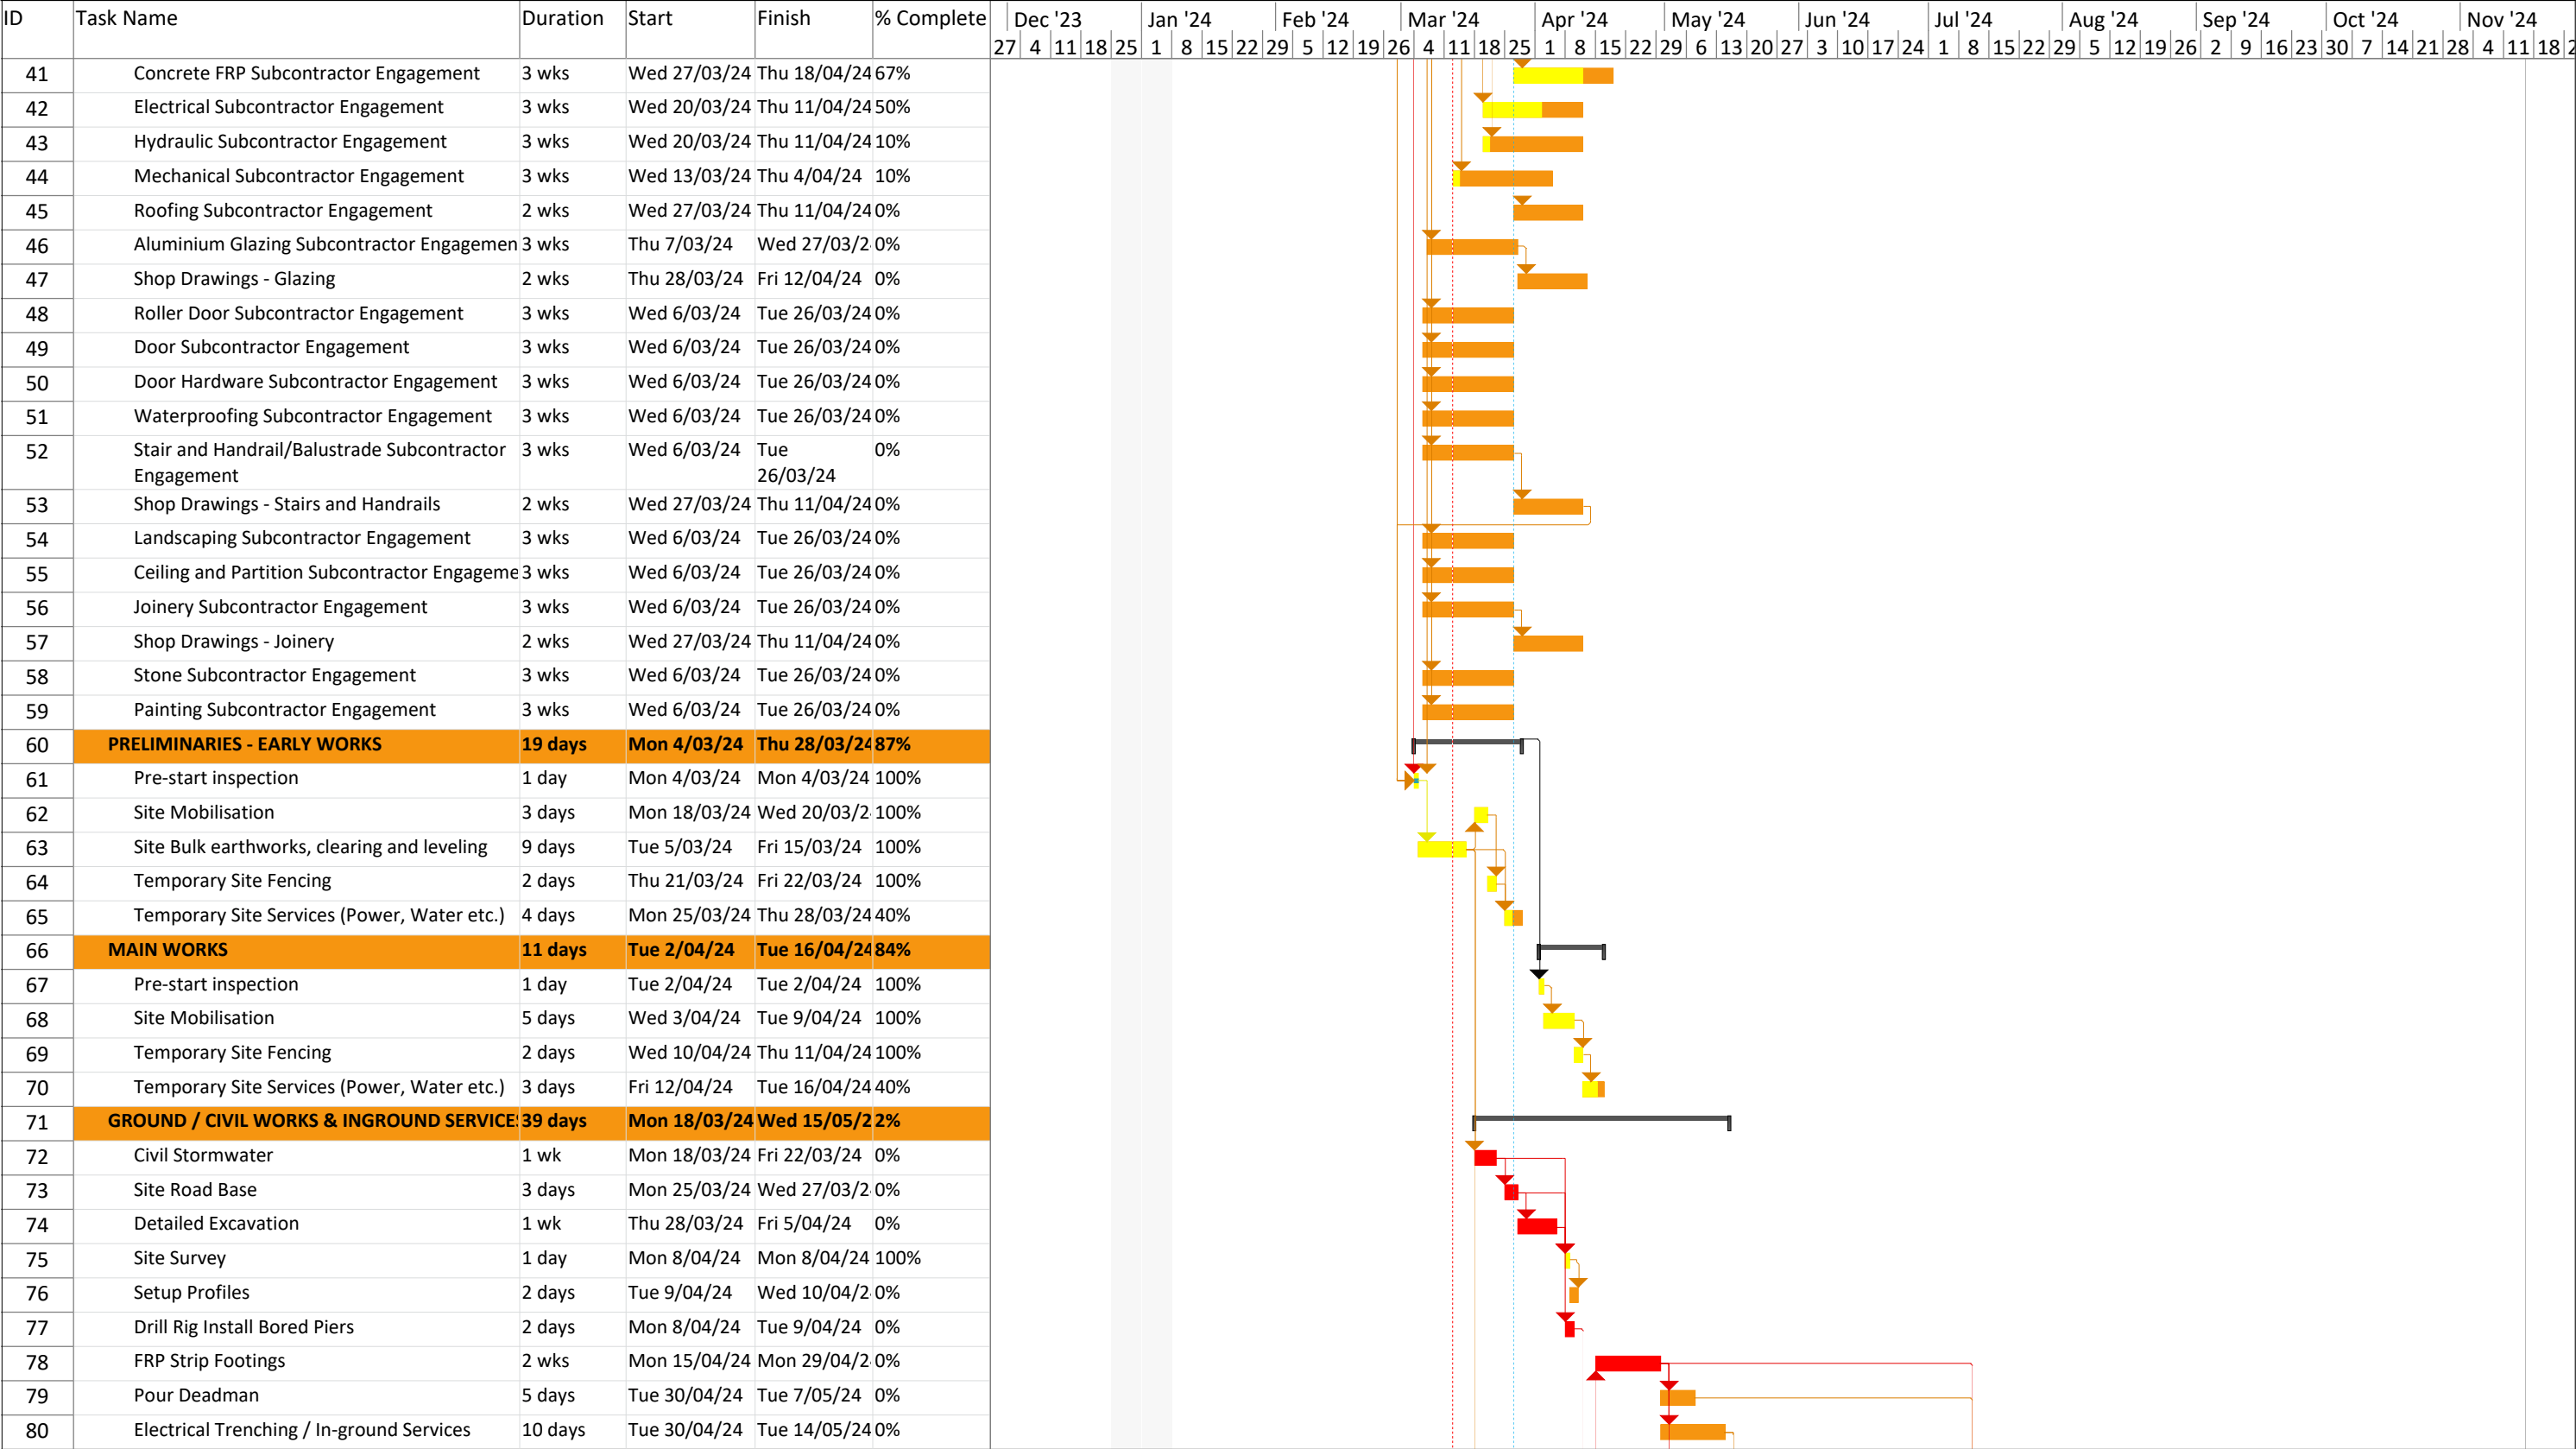

1-5 HOMESTEAD DRIVE, STAPYLTON
CONTRACT PROGRAMME

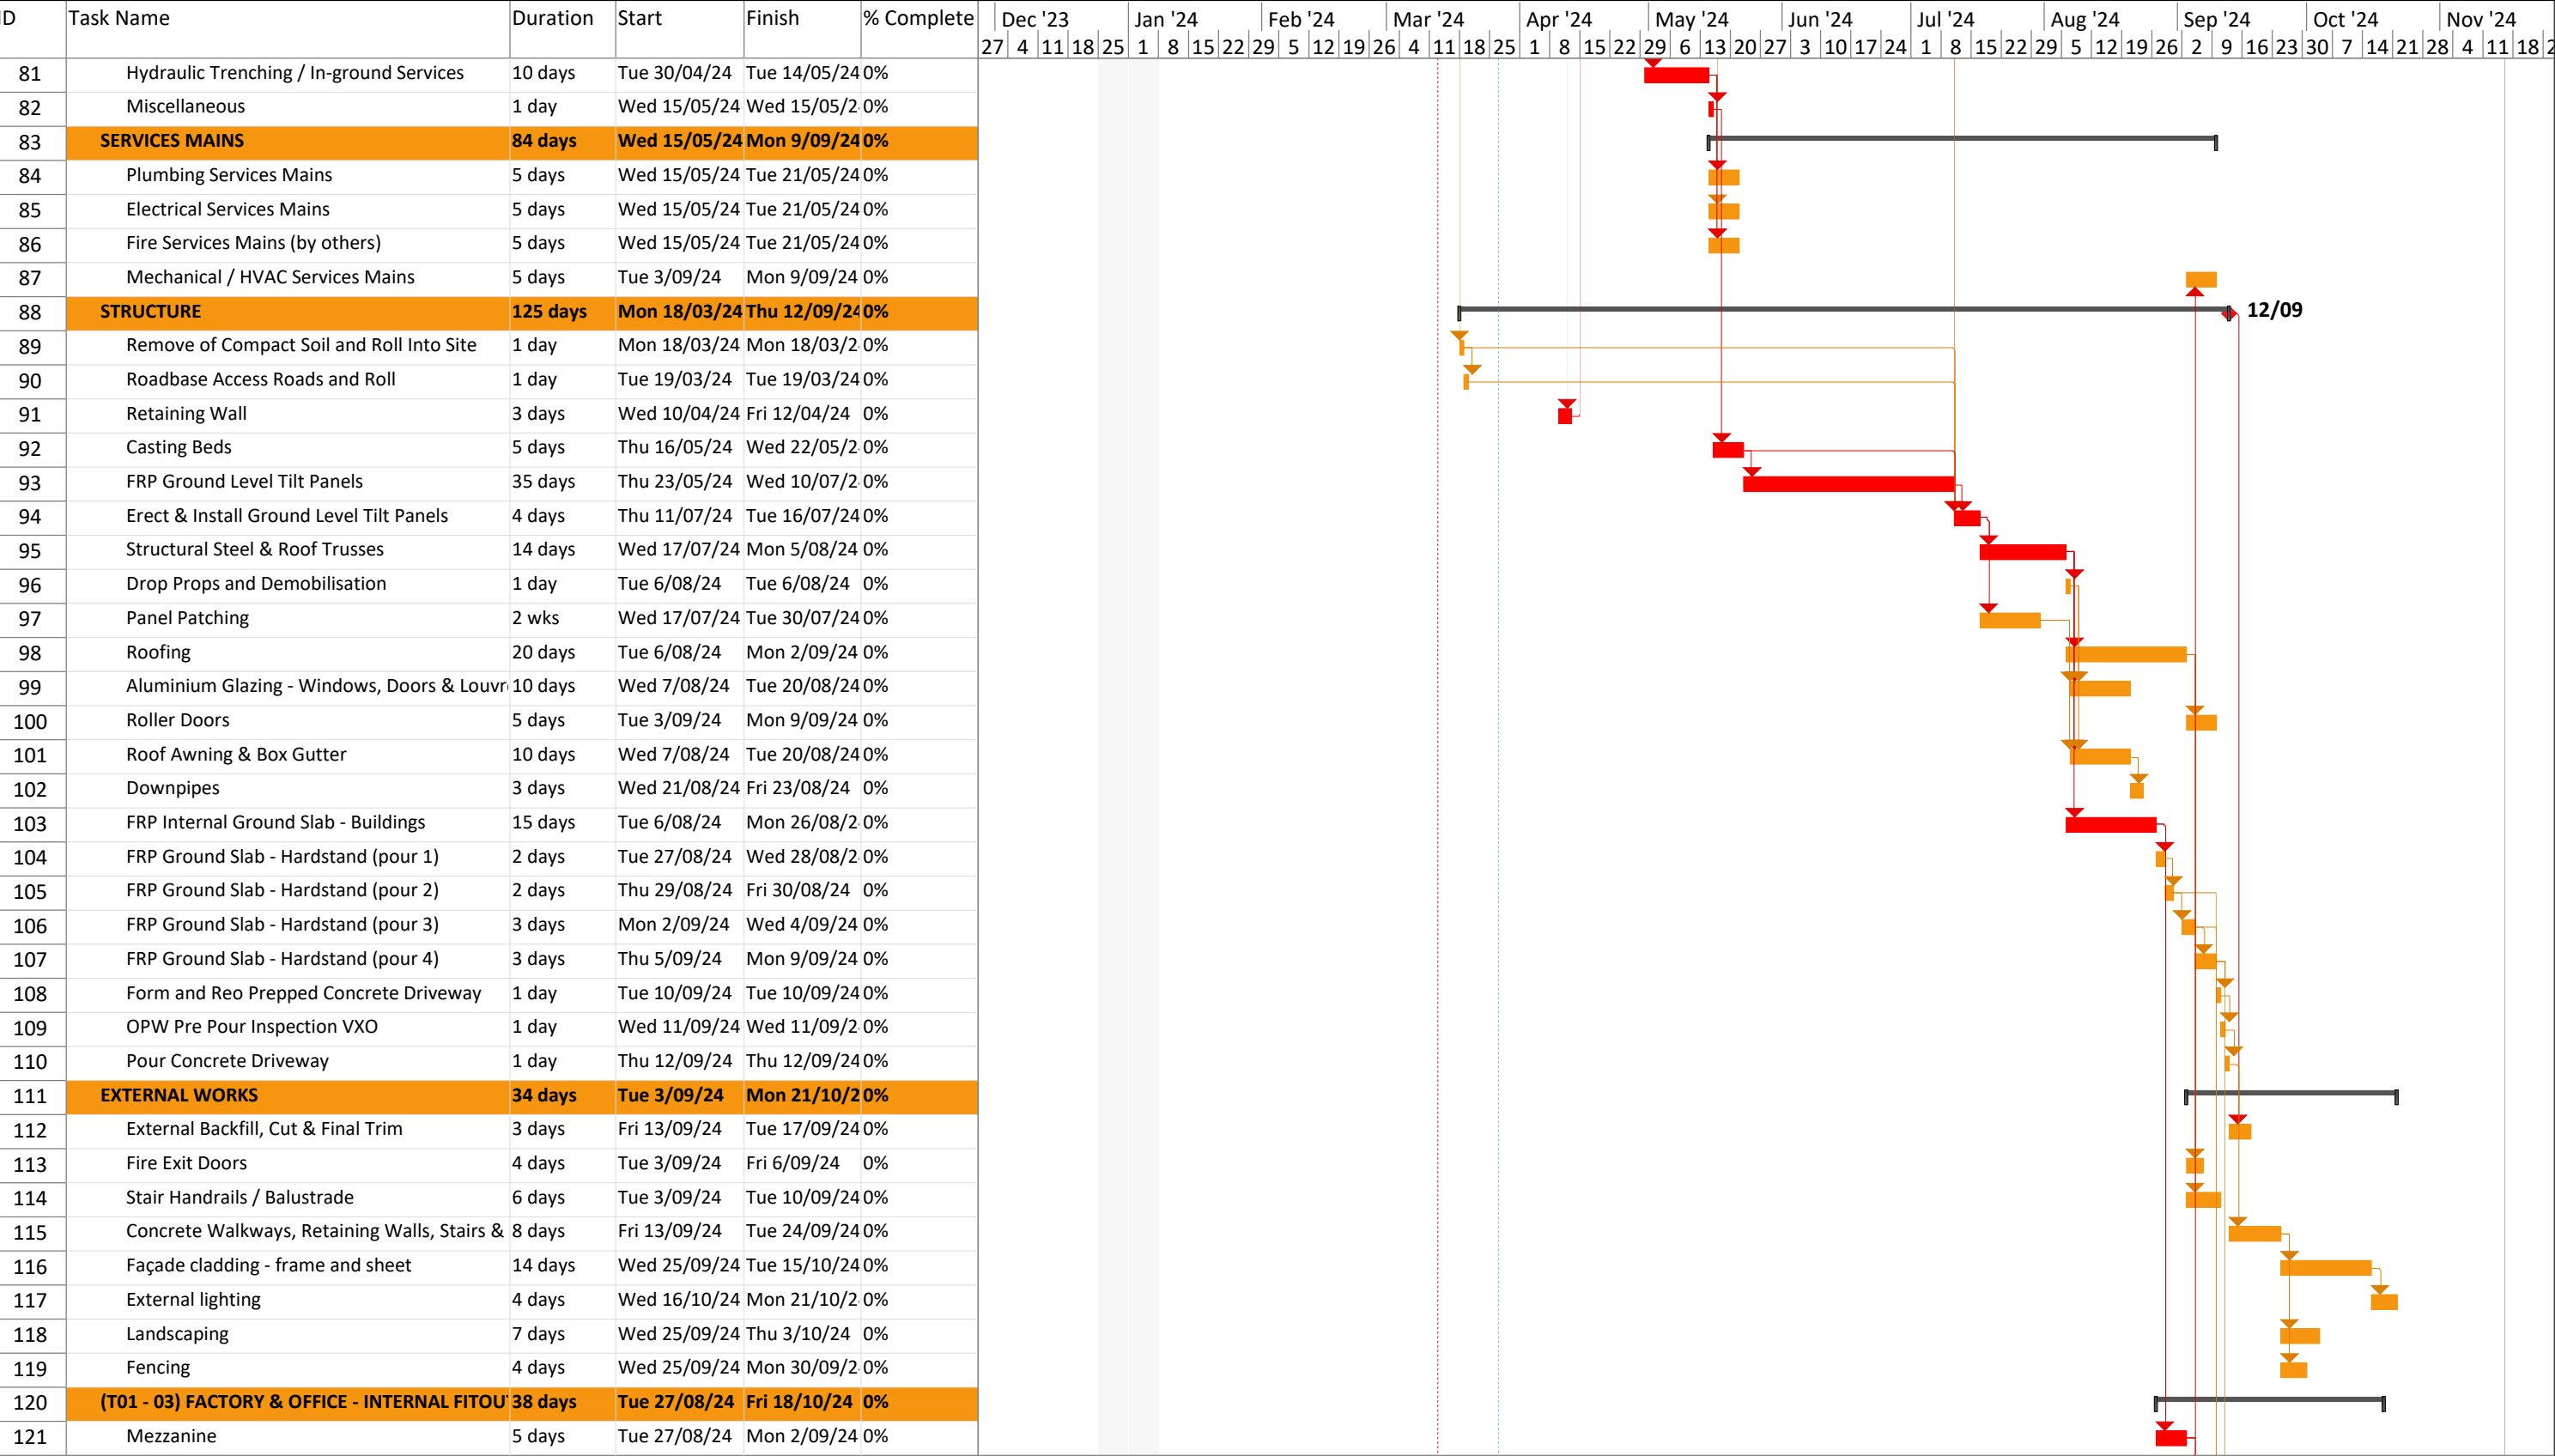

Date: 13.03.24
Planner: SD Checked: RM
Revision: Rev 2

1-5 HOMESTEAD DRIVE, STAPYLTON

CONTRACT PROGRAMME



ID	Task Name	Duration	Start	Finish	% Complete
122	Perimeter Wall Stud Framing	3 days	Tue 3/09/24	Thu 5/09/24	0%
123	Ceiling Grid Setout	3 days	Fri 6/09/24	Tue 10/09/24	0%
124	Internal Stud Framing	2 days	Wed 11/09/24	Thu 12/09/24	0%
125	Plumbing Services - Rough In	2 days	Fri 13/09/24	Mon 16/09/24	0%
126	Electrical Services - Rough In	2 days	Fri 13/09/24	Mon 16/09/24	0%
127	Mechanical Services - Rough In	3 days	Fri 13/09/24	Tue 17/09/24	0%
128	Aluminium Door Frames	3 days	Wed 11/09/24	Fri 13/09/24	0%
129	Wet Area Wall Sheeting	5 days	Tue 17/09/24	Mon 23/09/24	0%
130	Wet Area Wall Set & Sand	1 day	Mon 23/09/24	Mon 23/09/24	0%
131	Wet Area Screeding & Waterproofing	4 days	Tue 24/09/24	Fri 27/09/24	0%
132	Wet Area Tiling	4 days	Mon 30/09/24	Thu 3/10/24	0%
133	Joinery & Stone	3 days	Fri 13/09/24	Tue 17/09/24	0%
134	Internal Wall sheeting	5 days	Tue 24/09/24	Mon 30/09/24	0%
135	Doors & Door Hardware	3 days	Tue 1/10/24	Thu 3/10/24	0%
136	Internal Painting	5 days	Tue 1/10/24	Tue 8/10/24	0%
137	Plumbing Final Fix	3 days	Wed 16/10/24	Fri 18/10/24	0%
138	Electrical Final Fix	3 days	Wed 16/10/24	Fri 18/10/24	0%
139	Mechanical Final Fix	3 days	Tue 24/09/24	Thu 26/09/24	0%
140	Signage	3 days	Wed 16/10/24	Fri 18/10/24	0%
141	Floor Coverings	3 days	Fri 4/10/24	Wed 9/10/24	0%
142	Miscellaneous Works	1 day	Thu 10/10/24	Thu 10/10/24	0%
143	(T04 - 06) FACTORY & OFFICE - INTERNAL FITOUT	38 days	Fri 30/08/24	Wed 23/10/24	0%
144	Mezzanine	6 days	Fri 30/08/24	Fri 6/09/24	0%
145	Perimeter Wall Stud Framing	4 days	Wed 4/09/24	Mon 9/09/24	0%
146	Ceiling Grid Setout	4 days	Mon 9/09/24	Thu 12/09/24	0%
147	Internal Stud Framing	2 days	Fri 13/09/24	Mon 16/09/24	0%
148	Plumbing Services - Rough In	3 days	Tue 17/09/24	Thu 19/09/24	0%
149	Electrical Services - Rough In	3 days	Tue 17/09/24	Thu 19/09/24	0%
150	Mechanical Services - Rough In	3 days	Wed 18/09/24	Fri 20/09/24	0%
151	Aluminium Door Frames	3 days	Mon 16/09/24	Wed 18/09/24	0%
152	Wet Area Wall Sheeting	5 days	Tue 24/09/24	Mon 30/09/24	0%
153	Wet Area Wall Set & Sand	1 day	Tue 24/09/24	Tue 24/09/24	0%
154	Wet Area Screeding & Waterproofing	4 days	Mon 30/09/24	Thu 3/10/24	0%
155	Wet Area Tiling	4 days	Fri 4/10/24	Thu 10/10/24	0%
156	Joinery & Stone	3 days	Wed 18/09/24	Fri 20/09/24	0%
157	Internal Wall sheeting	5 days	Tue 1/10/24	Tue 8/10/24	0%
158	Doors & Door Hardware	3 days	Fri 4/10/24	Wed 9/10/24	0%
159	Internal Painting	5 days	Wed 9/10/24	Tue 15/10/24	0%
160	Plumbing Final Fix	3 days	Mon 21/10/24	Wed 23/10/24	0%
161	Electrical Final Fix	3 days	Mon 21/10/24	Wed 23/10/24	0%
162	Mechanical Final Fix	3 days	Fri 27/09/24	Tue 1/10/24	0%

Project: 1-5 HOMESTEAD DRIVE C
Date: Wed 13/03/24

Task		Summary		Critical
Milestone		Project Summary		Progress

Page 4

1-5 HOMESTEAD DRIVE, STAPYLTON
CONTRACT PROGRAMME

